


Biweekly Municipality Report

District	Municipality	Ward	VDC	Total Beneficiary	Date
Gorkha	Barpak Sulikot Rural Municipality	-	-	7,020	5/31

1. Housing Reconstruction Status

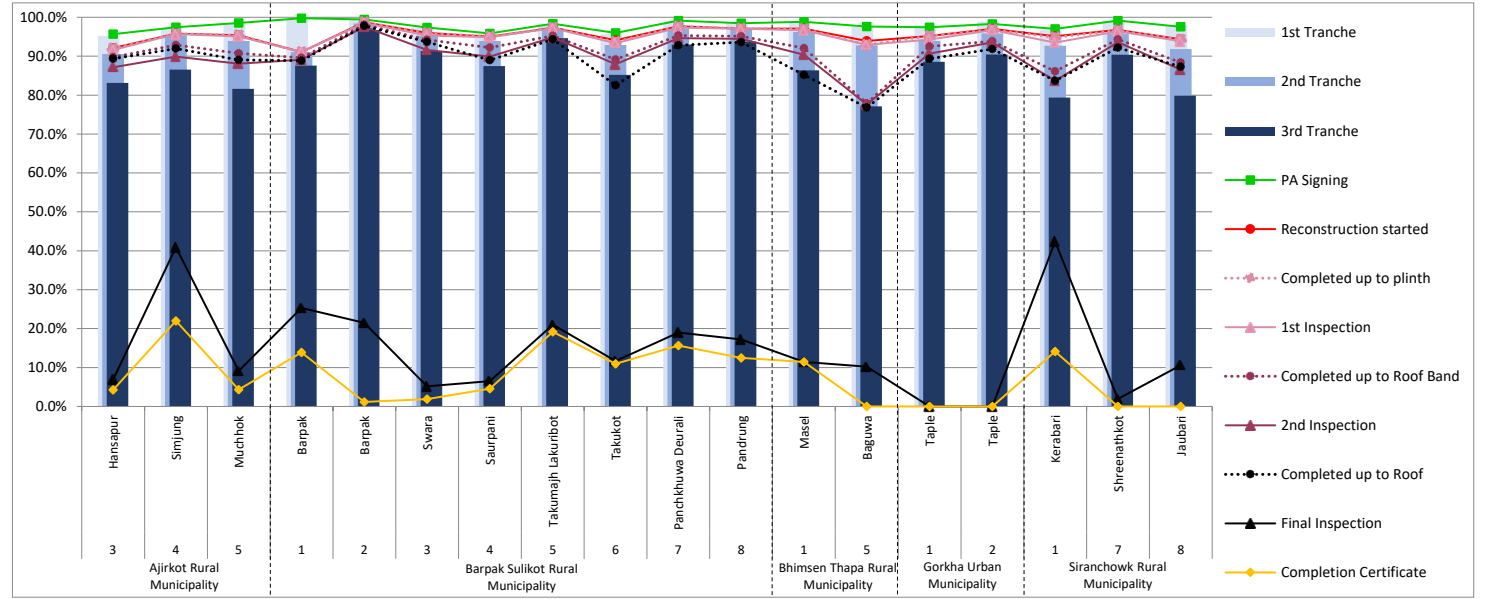

2. Progress

Reconstruction Flow	Previous Period		This Period		Increase/Decrease	
	5/15		5/31			
	%	No	%	No	%	No
PA Signing	97.6%	6,850	97.6%	6,850	0.0%	-
1st Tranche	97.5%	6,841	97.5%	6,845	0.1%	4
Reconstruction started	95.8%	6,727	95.9%	6,735	0.1%	8
Completed up to plinth	95.8%	6,722	95.9%	6,731	0.1%	9
1st Inspection	95.6%	6,708	95.7%	6,715	0.1%	7
2nd Tranche	94.8%	6,658	95.3%	6,689	0.4%	31
Completed up to Roof Band	93.2%	6,542	93.5%	6,566	0.3%	24
2nd Inspection	92.0%	6,455	92.2%	6,471	0.2%	16
3rd Tranche	89.6%	6,289	90.7%	6,368	1.1%	79
Completed up to Roof	90.6%	6,359	91.2%	6,401	0.6%	42
Final Inspection	12.4%	873	13.7%	963	1.3%	90
Completion Certificate	6.4%	451	8.4%	587	1.9%	136

3. Stage and Status

Categories of issue		No. of beneficiary				Remark
		Previous	This Time			
			Total	Unsolved	New	
A	~PA Not Signed	170	133	37	170	
	a_First access	-	-	-	-	
	a_Out of contact	21	9	-	9	
	a_Beneficiary Duplication	61	58	19	77	Letter forwarded to GMaLI (0522)
	a_Document insufficient	3	3	1	4	
	a_Death	12	12	-	12	
	a_Migrated elsewhere	6	5	1	6	
	a_Landless	2	2	-	2	
	a_Resettlement beneficiary	-	-	-	-	
	a_Not Interested	20	15	9	24	
	a_Unknown Beneficiary	18	3	-	3	
	a_Affected by Right of Way	-	-	-	-	
	a_Insufficient/Unsuitable Land	-	-	-	-	
	a_Beneficiary supported by other program	22	22	-	22	
	a_Deadline expired	-	-	-	-	
	a_Others	5	4	7	11	
B	PA Signed~1st Tranche not deposited	12	2	3	5	
	b_On Schedule (No action required)	6	1	-	1	
	b_Pending in Ward office	3	1	1	2	
	b_Pending in DLPIU (GMaLI)	-	-	-	-	
	b_Others	3	-	2	2	
C	1st Tranche deposited~ Not Started	144	94	19	113	
	c_On Schedule (No action required)	44	21	11	32	
	c_Death	11	11	-	11	
	c_Landless	-	-	-	-	
	c_Affected by Right of way	1	1	-	1	
	c_Resettlement beneficiary	24	20	-	20	
	c_Inaccessible	-	-	-	-	
	c_Will not construct	19	6	-	6	
	c_Willing to refund grant	3	3	2	5	
	c_Already refunded grant	-	-	-	-	
	c_Out of contact	10	6	-	6	
	c_Migrated to other place	4	4	-	4	
	c_Poor economic condition	2	-	-	-	
	c_No immediate plan to construct	6	5	2	7	
	c_Building permit not completed	-	-	-	-	
	c_Family Issues	-	-	-	-	
	c_Responsible person out of house	17	14	-	14	
	c_Cultural Taboos	-	-	1	1	
	c_Conversion from RCB to RTB	-	-	-	-	
	c_1st Tranche deposited without PA sign	-	-	2	2	
	c_Delayed due to Integrated Settlement decision	-	-	-	-	
	c_Indecisive NGO support	1	1	-	1	
	c_Document insufficient to withdraw grant	-	-	-	-	
	c_Others	2	2	1	3	
D	Started~Plinth Not Completed	3	1	3	4	
	d_On Schedule (No action required)	2	-	2	2	
	d_Poor economic condition	-	-	-	-	
	d_Death	-	-	-	-	
	d_Land Dispute	-	-	-	-	
	d_Family Issues	-	-	-	-	
	d_Migrated to other place	-	-	-	-	
	d_Will not continue	1	1	1	2	
	d_Out of contact	-	-	-	-	
	d_Delayed due to Integrated Settlement decision	-	-	-	-	
	d_Delayed by contractor	-	-	-	-	
	d_Lack of Mason	-	-	-	-	
	d_Others	-	-	-	-	

E	Plinth completed ~ 1st Inspection not conducted	20	2	14	16
	e_On Schedule (No action required)	12	-	11	11
	e_DLPIU engineer not available	5	-	2	2
	e_Non compliance	2	2	-	2
	e_Constructed in public land	-	-	-	-
	e_Affected by Right of Way	-	-	-	-
	e_Out of contact	-	-	1	1
	e_Others	1	-	-	-
F	1st Inspection conducted~2nd Tranche not deposited	82	10	14	24
	f_On Schedule (No action required)	56	8	12	20
	f_Pending in Ward office	14	-	-	-
	f_Rejected by DLPIU (Building)	2	1	-	1
	f_Rejected by DLPIU (GMaLI)	1	-	2	2
	f_Pending in DLPIU (Building)	7	1	-	1
	f_Pending in DLPIU (GMaLI)	1	-	-	-
	f_Suspended NGO Support	-	-	-	-
	f_Others	1	-	-	-
G	2nd Tranche deposited~Roof Band not completed	230	119	28	147
	g_On Schedule (No action required)	151	67	18	85
	g_Death	3	3	-	3
	g_Inaccessible	1	1	-	1
	g_Affected by Right of way	-	-	1	1
	g_Out of contact	2	-	-	-
	g_Migrated to other place	5	5	-	5
	g_Poor economic condition	25	13	1	14
	g_Will not continue	-	-	-	-
	g_No immediate plan to continue	11	9	2	11
	g_Family Issues	7	5	1	6
	g_Responsible person out of house	9	7	2	9
	g_Cultural Taboos	1	-	1	1
	g_Suspended NGO Support	-	-	-	-
	g_Delayed due to Integrated Settlement decision	-	-	-	-
	g_Delayed by contractor	3	1	1	2
	g_Shortage of Materials	9	6	1	7
	g_Tranche deposited without required progress	-	-	-	-
	g_Document insufficient to withdraw grant	-	-	-	-
	g_Tranche deposited without compliance	-	-	-	-
	g_Lack of Mason	-	-	-	-
	g_Lack of Carpenter	-	-	-	-
	g_Others	3	2	-	2
H	Roof Band Completed~2nd Inspection not conducted	229	26	55	81
	h_On Schedule (No action required)	147	14	47	61
	h_DLPIU engineer not available	20	1	1	2
	h_Non compliance	14	6	1	7
	h_Toilet/ Renewable energy not constructed	42	5	6	11
	h_Electric Meter not installed	-	-	-	-
	h_Affected by Right of Way	-	-	-	-
	h_Out of contact	4	-	-	-
	h_Additional requirement of roof completion	2	-	-	-
	h_Others	-	-	-	-
I	2nd Inspection conducted ~3rd Tranche not deposited	361	27	65	92
	i_On Schedule (No action required)	247	13	57	70
	i_Pending in Ward office	74	8	-	8
	i_Rejected by DLPIU (Building)	11	2	5	7
	i_Rejected by DLPIU (GMaLI)	1	-	2	2
	i_Pending in DLPIU (Building)	28	4	1	5
	i_Pending in DLPIU (GMaLI)	-	-	-	-
	i_Suspended NGO Support	-	-	-	-
	i_Others	-	-	-	-

J	3rd Tranche deposited~Roof not completed	148	54	60	114	
	j_On Schedule (No action required)	109	40	60	100	
	j_Death	-	-	-	-	
	j_Inaccessible	-	-	-	-	
	j_Out of contact	-	-	-	-	
	j_Migrated to other place	-	-	-	-	
	j_Poor economic condition	3	2	-	2	
	j_No immediate plan to continue	5	3	-	3	
	j_Family Issues	1	1	-	1	
	j_Responsible person out of house	3	1	-	1	
	j_Cultural Taboos	2	2	-	2	
	j_Delayed due to Integrated Settlement decision	-	-	-	-	
	j_Delayed by contractor	-	-	-	-	
	j_Shortage of Materials	13	1	-	1	
	j_Lack of Carpenter	10	4	-	4	
	j_Tranche deposited without required progress	-	-	-	-	
	j_Tranche deposited without compliance	-	-	-	-	
	j_Document insufficient to withdraw grant	-	-	-	-	
	j_Lack of welder	-	-	-	-	
	j_Others	2	-	-	-	
K	Roof Completed~Final Inspection not conducted	4,972	4,200	1,091	5,291	
	k_On Schedule (No action required)	2,148	1,490	578	2,068	
	k_DLPIU engineer not available	434	433	455	888	
	k_Non compliance	100	98	5	103	
	k_Affected by Right of Way	1	1	-	1	
	k_Out of contact	3	2	-	2	
	k_Old house not demolished	282	280	5	285	
	k_Electric Meter not installed	-	-	-	-	
	k_Window or door not installed	1,920	1,848	47	1,895	
	k_Record keeping not completed	-	-	-	-	
	k_Building permit not completed	-	-	1	1	
	k_Others	84	48	-	48	
L	Final Inspection completed~Completion certificate not distributed	505	315	61	376	
	l_On Schedule (No action required)	456	315	54	369	
	l_Waiting for good quality certificate	49	-	-	-	
	l_Unavailability of Completion certificate	-	-	-	-	
	l_Record keeping not completed	-	-	-	-	
	l_Building permit not completed	-	-	-	-	
	l_Others	-	-	7	7	
M	Completion Certificate distributed	140	140	447	587	
	m_Without issue	140	140	447	587	
	m_Non compliance	-	-	-	-	
	Total	7,016	5,123	1,897	7,020	

4. DLPIU Engineers (deployed/allocated)

	Total		1		2		3		4		5		6		7		8		
	D	A	D	A	D	A	D	A	D	A	D	A	D	A	D	A	D	A	
Engineers	8	9	0.5	1	0.5	1	1	1	2	2	1	1	1	1	1	1	1	1	1
Sub-engineers	5	5	0	0	0	0	1	1	1	1	1	1	1	1	1	1	0	0	
Asst. Engineers	8	9	0.5	0.5	0.5	0.5	1	1	2	2	1	1	2	2	0	1	1	1	

(D: Deployed A: Allocated)

5. Priority Issue / Action Plan

Inspection and completion certificate
 >>Follow up for the 1st, 2nd and 3rd inspection and completion certificate
